


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Qtr 1, 2019			Qtr 2, 2019			Qtr 3, 2019			Qtr 4, 2019			Qtr 1, 2020			Qtr 2, 2020			Qtr 3, 2020			Qtr 4, 2020			Qtr 1, 2021									
							Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar						
1	📌	Notice to Proceed	0 days	Wed 1/1/20	Wed 1/1/20																																			
2	📌	<b>Stakeholder Coordination</b>	<b>506 days</b>	<b>Mon 2/4/19</b>	<b>Mon 1/11/21</b>																																			
3	📌	City of Bellaire Public Meeting No. 1	0 days	Mon 2/4/19	Mon 2/4/19																																			
4	📌	City of Bellaire Public Meeting No. 2	0 days	Fri 6/21/19	Fri 6/21/19	12FS+14 days																																		
5	📌	City of Bellaire Public Meeting No. 3	0 days	Mon 1/11/21	Mon 1/11/21	25																																		
6	📌	<b>Concept Development</b>	<b>69 days</b>	<b>Wed 1/1/20</b>	<b>Mon 4/6/20</b>																																			
7	📌	Preliminary Hydrologic & Hydarulic Evaluation	45 days	Wed 1/1/20	Tue 3/3/20	1																																		
8	📌	Project Concept Development	7 days	Mon 2/24/20	Tue 3/3/20	7FS-7 days																																		
9	📌	Initial Screening Workshop	0 days	Tue 3/10/20	Tue 3/10/20	8FS+5 days																																		
10	📌	Concept Design Memo - DRAFT	5 days	Wed 3/4/20	Tue 3/10/20	8																																		
11	📌	Review of Memo by Stakeholders (estimated)	14 days	Wed 3/11/20	Mon 3/30/20	10																																		
12	📌	Concept Design Memo-FINAL	5 days	Tue 3/31/20	Mon 4/6/20	11																																		
13	📌	<b>Master Drainage Concept Plan</b>	<b>269 days</b>	<b>Wed 1/1/20</b>	<b>Mon 1/11/21</b>																																			
14	📌	Data Collection	21 days	Wed 1/1/20	Wed 1/29/20	1																																		
15	📌	Topographic Surveying	45 days	Wed 1/1/20	Tue 3/3/20	1																																		
16	📌	Existing Condition H&H Analysis	90 days	Wed 1/1/20	Tue 5/5/20	1,14FF,15FF+20 d																																		
17	📌	Improvement Alternatives Development	60 days	Wed 5/6/20	Tue 7/28/20	16,12FF+7 days																																		
18	📌	Proposed Condition H&H Analysis	60 days	Wed 5/20/20	Tue 8/11/20	17SS+10 days																																		
19	📌	Alternatives Analysis	60 days	Wed 6/3/20	Tue 8/25/20	18SS+10 days																																		
20	📌	Schematic Layouts of Alternatives	25 days	Wed 7/1/20	Tue 8/4/20	18SS+20 days,19S																																		
21	📌	Cost Estimates	30 days	Wed 8/5/20	Tue 9/15/20	20																																		
22	📌	Develop Phasing Plan of Preferred Alternative	45 days	Wed 9/16/20	Tue 11/17/20	21,20,19																																		
23	📌	Prepare Technical Report	14 days	Thu 11/12/20	Tue 12/1/20	19,22FF+10 days																																		
24	📌	Review of Report by City of Bellaire, HCFC, and TxDOT	15 days	Wed 12/2/20	Tue 12/22/20	23																																		
25	📌	Finalize Technical Report	14 days	Wed 12/23/20	Mon 1/11/21	24																																		

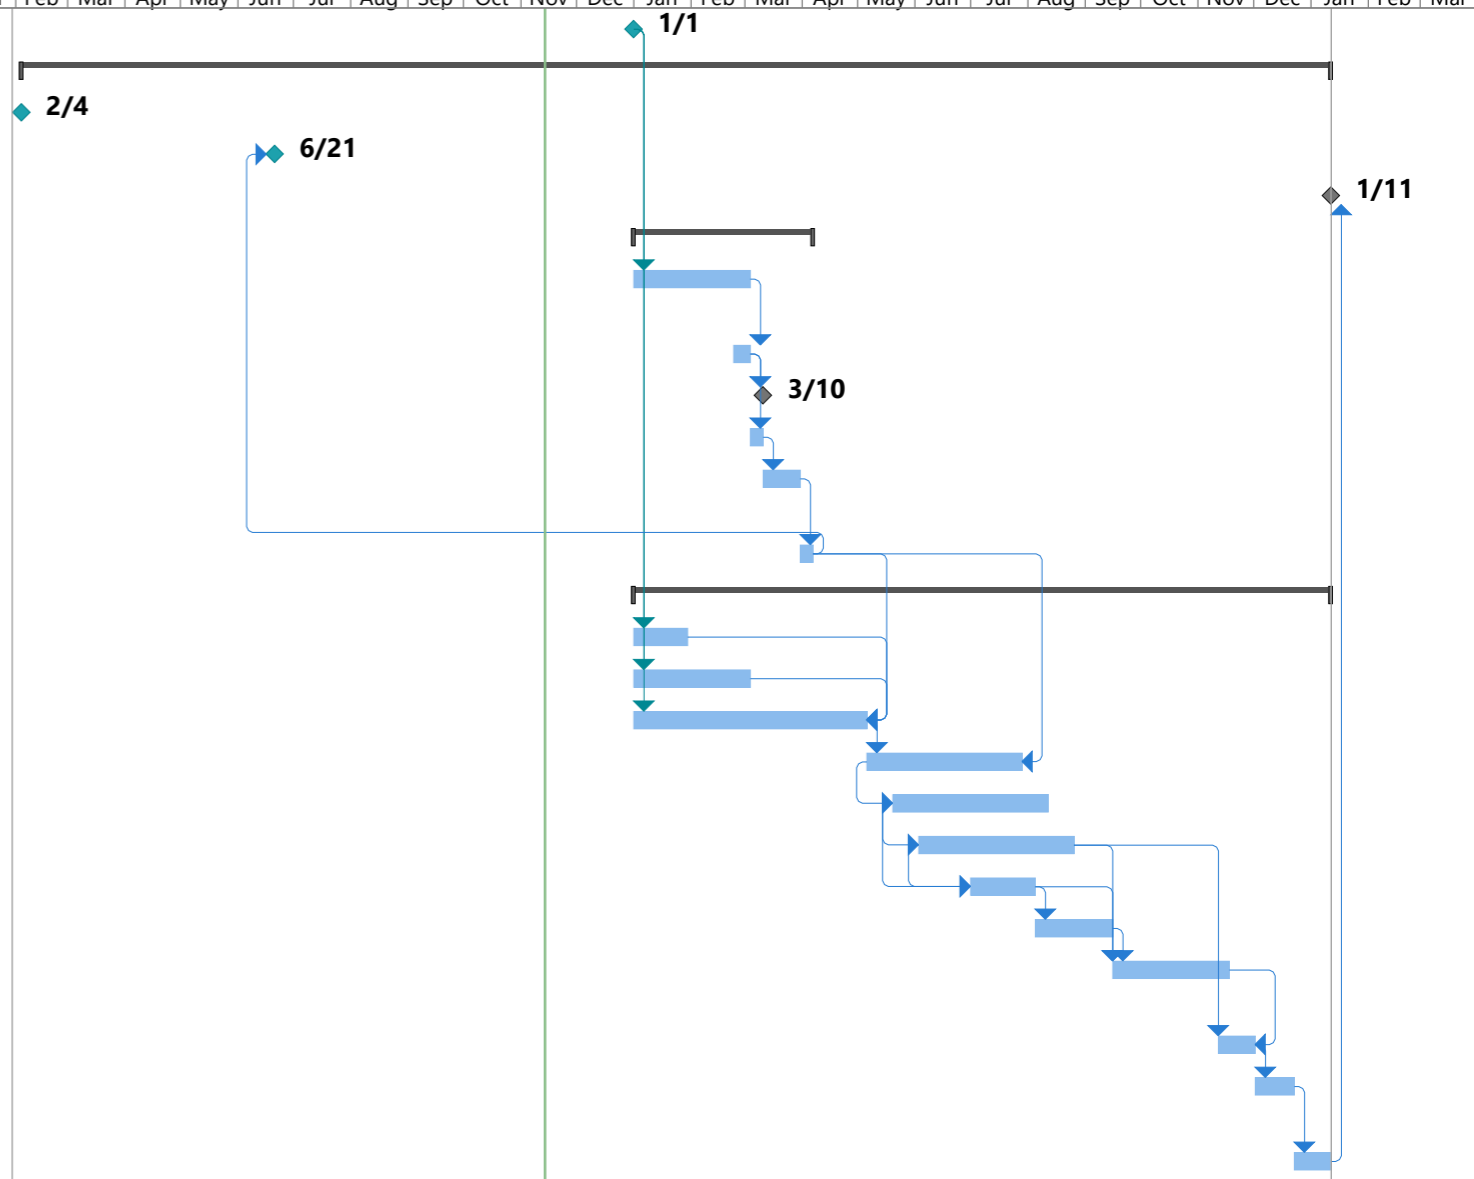

Project: MDCP-Schedule Date: Thu 11/14/19	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
