


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Qtr 1, 2020			Qtr 2, 2020			Qtr 3, 2020			Qtr 4, 2020			Qtr 1, 2021		
							Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
1		Notice to Proceed	0 days	Wed 1/1/20	Wed 1/1/20		1/1														
2		<b>Stakeholder Coordination</b>	<b>285 days</b>	<b>Tue 2/4/20</b>	<b>Mon 3/8/21</b>																
3		City of Bellaire Public Meeting No. 1	0 days	Tue 2/4/20	Tue 2/4/20			2/4													
4		City of Bellaire Public Meeting No. 2	0 days	Sun 6/21/20	Sun 6/21/20	12FS+14 days															
5		City of Bellaire Public Meeting No. 3	0 days	Mon 3/8/21	Mon 3/8/21	25															
6		<b>Concept Development</b>	<b>76 days</b>	<b>Tue 2/18/20</b>	<b>Tue 6/2/20</b>																
7		Preliminary Hydrologic & Hydarulic Evaluation	45 days	Tue 2/18/20	Mon 4/20/20	1															
8		Project Concept Development	7 days	Tue 4/21/20	Wed 4/29/20																
9		Initial Screening Workshop	0 days	Wed 5/6/20	Wed 5/6/20	8FS+5 days															
10		Concept Design Memo - DRAFT	5 days	Thu 4/30/20	Wed 5/6/20	8															
11		Review of Memo by Stakeholders (estimated)	14 days	Thu 5/7/20	Tue 5/26/20	10															
12		Concept Design Memo-FINAL	5 days	Wed 5/27/20	Tue 6/2/20	11															
13		<b>Master Drainage Concept Plan</b>	<b>309 days</b>	<b>Wed 1/1/20</b>	<b>Mon 3/8/21</b>																
14		Data Collection	21 days	Wed 1/1/20	Wed 1/29/20	1															
15		Topographic Surveying	45 days	Wed 1/1/20	Tue 3/3/20	1															
16		Existing Condition H&H Analysis	90 days	Wed 2/26/20	Tue 6/30/20	1,14FF,15FF+20 d															
17		Improvement Alternatives Development	60 days	Wed 7/1/20	Tue 9/22/20	16,12FF+7 days															
18		Proposed Condition H&H Analysis	60 days	Wed 7/15/20	Tue 10/6/20	17SS+10 days															
19		Alternatives Analysis	60 days	Wed 7/29/20	Tue 10/20/20	18SS+10 days															
20		Schematic Layouts of Alternatives	25 days	Wed 8/26/20	Tue 9/29/20	18SS+20 days,19S															
21		Cost Estimates	30 days	Wed 9/30/20	Tue 11/10/20	20															
22		Develop Phasing Plan of Preferred Alternative	45 days	Wed 11/11/20	Tue 1/12/21	21,20,19															
23		Prepare Technical Report	14 days	Thu 1/7/21	Tue 1/26/21	19,22FF+10 days															
24		Review of Report by City of Bellaire, HCFC, and TxDOT	15 days	Wed 1/27/21	Tue 2/16/21	23															
25		Finalize Technical Report	14 days	Wed 2/17/21	Mon 3/8/21	24															

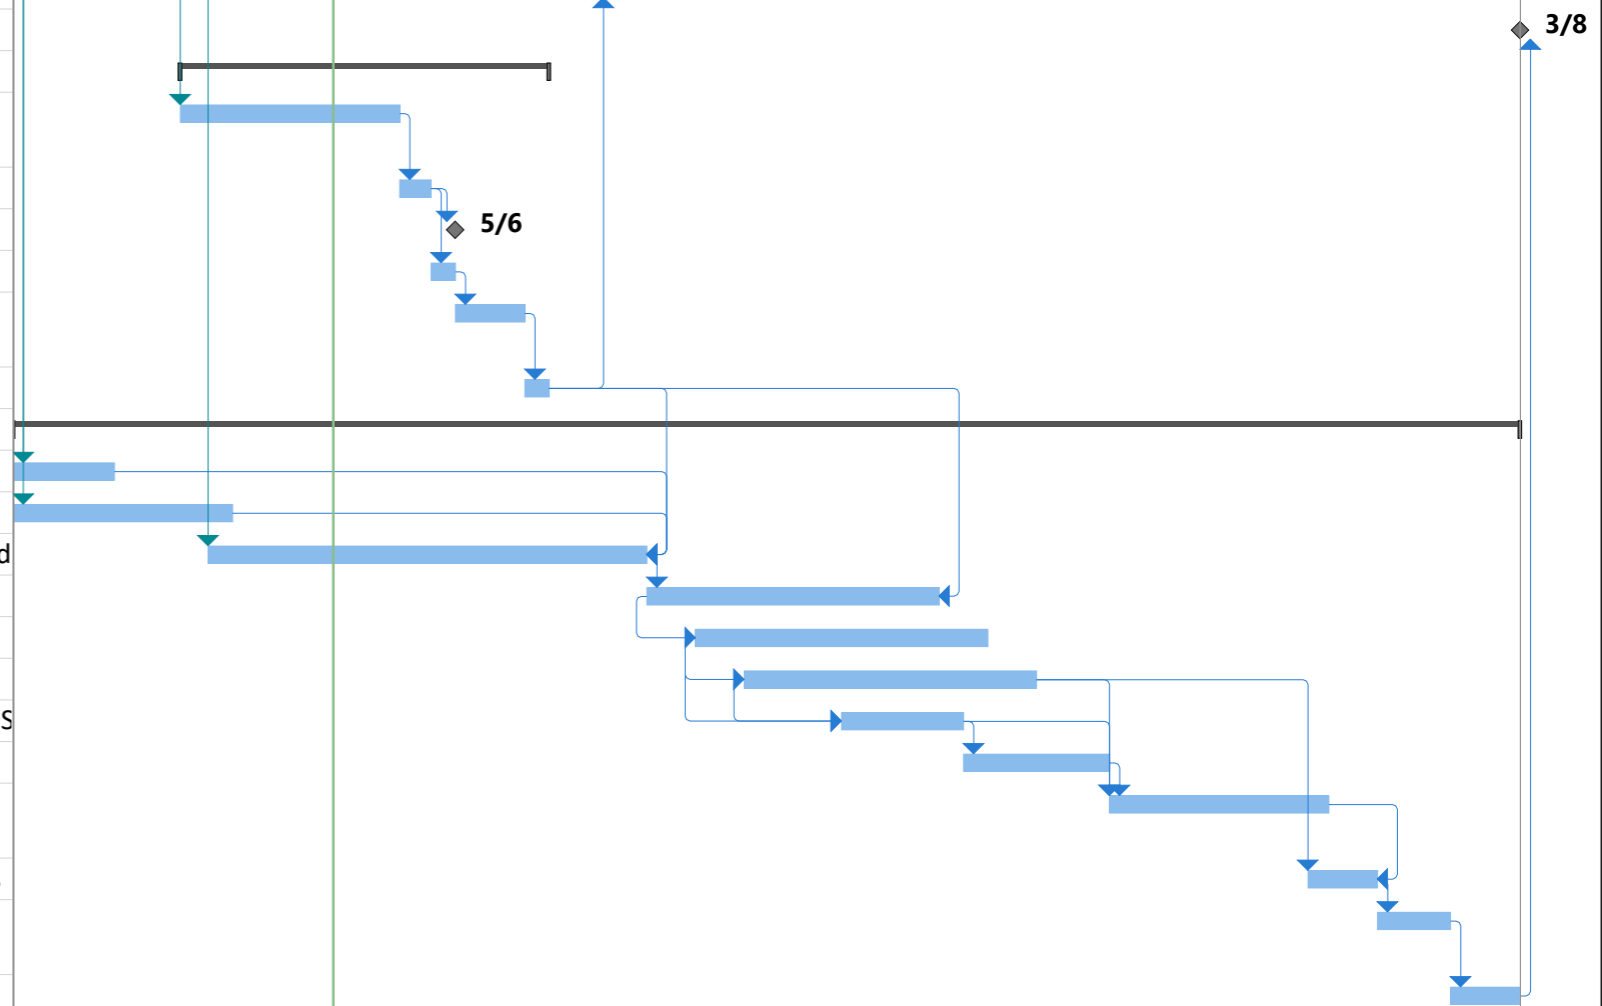

Project: MDCP-Schedule  
Date: Thu 4/2/20

Task		Project Summary		Manual Task		Start-only		External Tasks		Manual Progress		Deadline
Split		Inactive Task		Duration-only		Finish-only		External Milestone		Manual Progress		Progress
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		External Milestone		Manual Progress		Progress
Summary		Inactive Summary		Manual Summary		External Milestone		External Milestone		Manual Progress		Progress
